
Amendment to Intelligent Transit Management System Agreement and Project Status Report



Project Objectives

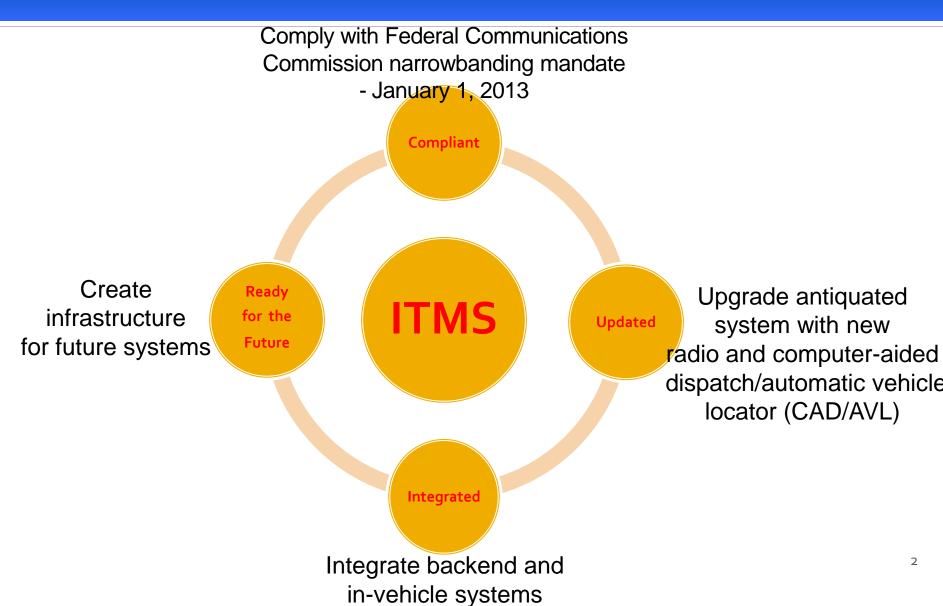

Project History

Actions Taken	2006				2007				2008				2009				2010				2011				2012			
	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
EIGER TechSystems conducts study																												
EIGER TechSystems completes study																												
Board approves ITMS project																												
Contracts Administration and Materials Management (CAMM) issues sole source contract with Affiliated Computer Services (ACS) – complete negotiations																												
Board approves sole source contract with ACS																												
Project kick off – begin development																												
ITMS projected completion																												

Completed Tasks

On-Going Tasks

Reporting Period

Tasks Completed, On-Going, and Scheduled during the reporting period

Milestone Tasks	October 2011			November 2011				December 2011				January 2012				February 2012				March 2012				
Continue factory acceptance testing (reregistration, affliation, fail over, silent alarm system voice and data issue)																								
Antenna installed at Santiago																								
Microwave installation at Construction Circle, Loma Ridge and Garden Grove																								
Contract amendment to include automated voice annunciation																								
Fixed end equipment delivery and installation																								
Optimize and test radio coverage																								

Installation of antenna at Santiago



Major Project Issues

Technical Issues

- ✓ Fail over automatic switching to backup system when primary system fails
- Silent alarm system simultaneous voice and data transmission when silent alarm is activated
- ✓ Affiliation time to register to new talk group
- Re-registration time to register back to previous channel when search for other channel fails


Project schedule

Delay in completing factory acceptance testing for six months impacts project completion date

Actions Taken by OCTA Project Team

- Met with Legal, CAMM and EIGER to define OCTA position on Article 1.2 of the scope of work
- Met with ACS to clarify OCTA position on Article 1.2 of the scope of work
- Identify which features in the old system should be included in the new system

Project Key Milestones Schedule/Budget

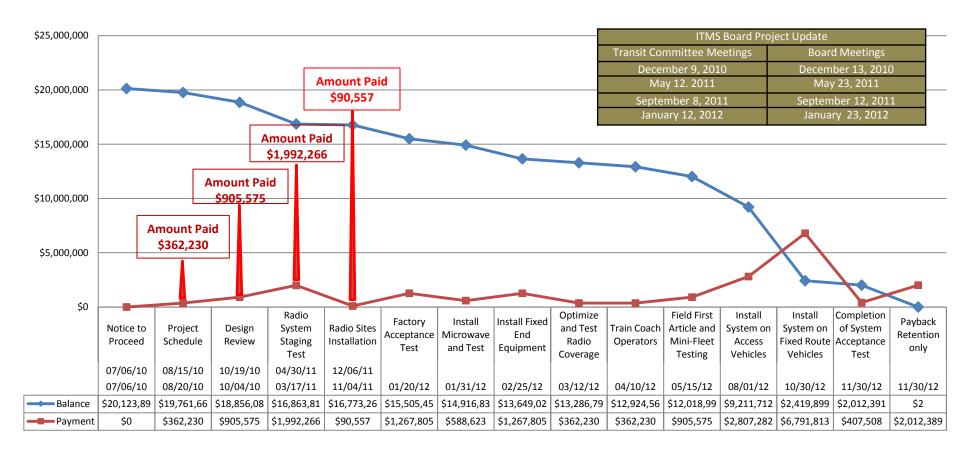

ITMS Revised Projected Completion Date – November 30, 2012 FCC Narrow banding – January, 2013

- To be paid at the completion of task
