

Update on the Interstate 5 Improvement Project Between State Route 73 and El Toro Road




Project Update

March 11, 2024



Project Overview

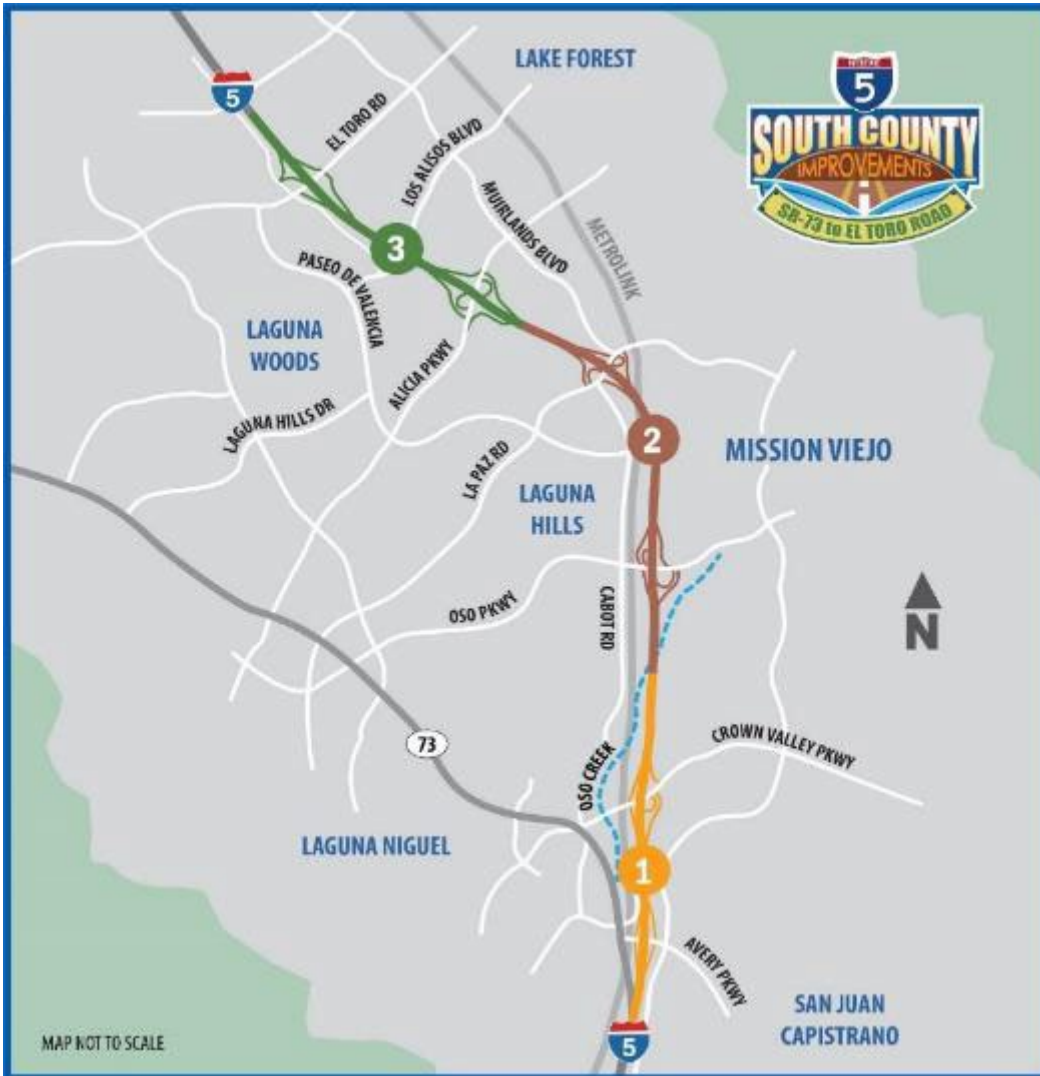

Segment ①

State Route 73 to Oso Parkway

Segment ②

Oso Parkway to Alicia Parkway

Segment ③

Alicia Parkway to El Toro Road

Total Length: 6.5 miles

Total Estimated Cost: \$664 million



Major Project Improvements

- 1** Add one general purpose lane in both directions from Avery Parkway to Alicia Parkway
- 2** Extend second carpool lane in both directions from Alicia Parkway to El Toro Road and restripe for continuous access
- 3** Reconstruct Avery Parkway and La Paz Road interchanges and Los Alisos Boulevard overcrossing
- 4** Reconstruct and add auxiliary lanes
- 5** Realign and improve on- and off-ramps

Estimated Construction Schedule

Segment	Estimated Schedule
<p>Segment 1 State Route 73 to Oso Parkway</p>	<p>February 2020 – Early 2025 <i>Construction is 90 percent complete</i></p>
<p>Segment 2 Oso Parkway to Alicia Parkway</p>	<p>May 2019 – Late 2024 <i>Construction is 92 percent complete</i></p>
<p>Segment 3 Alicia Parkway to El Toro Road</p>	<p>January 2021 – Late 2024 <i>Construction is 87 percent complete</i></p>

Interstate 5 (I-5) at Avery Parkway Interchange




I-5 at Crown Valley Parkway



I-5 at Oso Parkway



I-5 at La Paz Road



I-5 at Alicia Parkway



Los Alisos Boulevard Bridge



Aliso Creek Bike and Hiking Trail



I-5 at El Toro Road



I-5 Looking South Towards Los Alisos Bridge



Community Engagement



OC I-5 South County
Published by Later - January 2 at 5:00 PM

UPDATED: Attention South County! The I-5 Alicia Parkway straight southbound on-ramp closure has been postponed and will now close at 10 p.m. on Tuesday, Jan. 9 for roadway reconstruction and paving. The ramp will reopen at 8 a.m. on Saturday, Jan. 13.

Detour signs will be in place to assist motorists. Plan for additional travel time and any detours within the area. The schedule is subject to change due to inclement weather or unforeseen operational issues. For the latest upd... [See more](#)

EXTENDED RAMP CLOSURE

NEW TIMES
I-5 Alicia Pkwy SB Straight On-Ramp
10 p.m. Tuesday, Jan. 9 - 8 a.m. Saturday, Jan. 13

See insights and ads Boost again

88 likes 23 comments 22 shares

Like Comment Share

WEEKEND RAMP CLOSURE
I-5 El Toro Road Southbound Off-Ramp Closed

Dear Neighbor,
The I-5 El Toro Road southbound off-ramp will be closed for roadway reconstruction starting Friday, Jan. 19. The ramp will be closed over the weekend and will reopen Monday morning, Jan. 22.

WHEN:
I-5 El Toro Road southbound off-ramp closed
11 p.m. Friday, Jan. 19 - 5 a.m. Monday, Jan. 22

WHAT TO EXPECT:
Plan for additional travel time through the area.
Detour signs will be in place to assist motorists.
The schedule is subject to change due to inclement weather or unforeseen operational issues.

To see the latest construction updates, [SCAN HERE](#)

For additional project information, please visit octa.net/i5southcounty

STAY INFORMED

Outreach Team Contact Information



octa.net/i5SouthCounty



i5SouthCounty@octa.net



[@OCi5SouthCounty](https://www.instagram.com/OCi5SouthCounty)



[Facebook.com/OCi5SouthCounty](https://www.facebook.com/OCi5SouthCounty)



949-614-0202
(English/Español)

THANK YOU

