




Orangethorpe Railroad Corridor Grade Separation Program Update



Grade Separation Locations

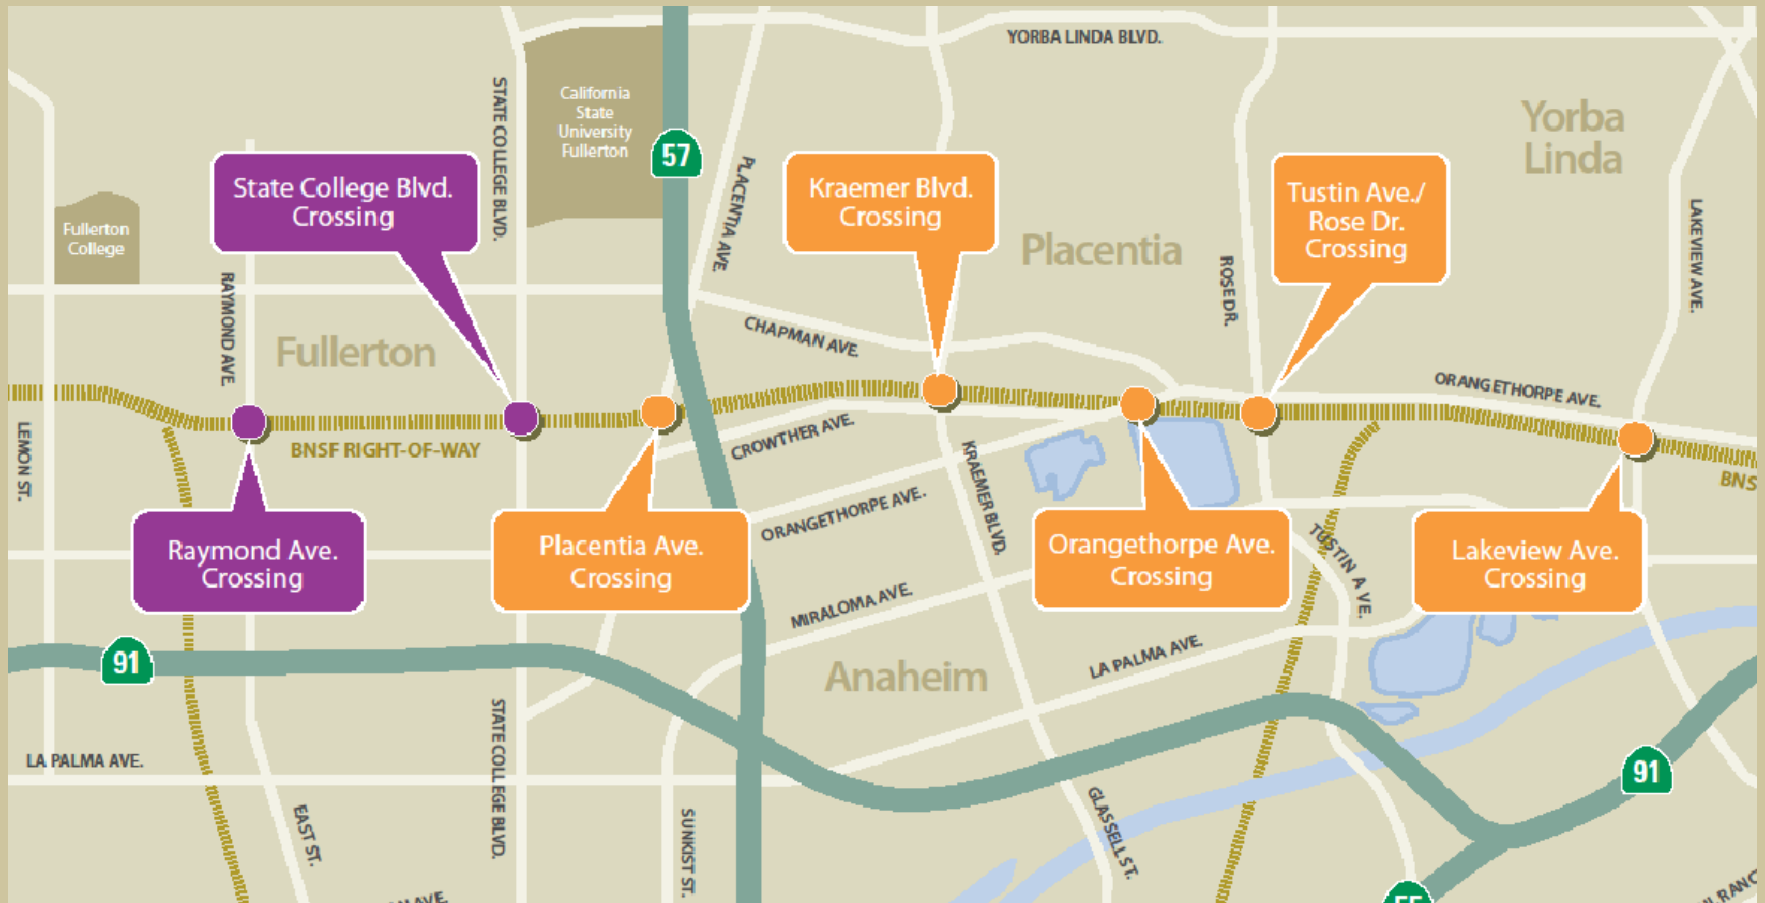

Program Schedule




Revised Railroad Grade Separation Program Schedule

November 7, 2011

| Location | UH /OC | Lead Agency | 2011 | 2012 | 2013 | 2014 | 2015 | 2016 |
|--------------------------|--------|-------------|--|--|--------------|--------------|--------------|--------------|
| Raymond Avenue | UC | Fullerton | Final Design, ROW Acquisition and Utility Relocation | Final Design, ROW Acquisition and Utility Relocation | Bid | Construction | Construction | Construction |
| State College Boulevard | UC | Fullerton | Final Design, ROW Acquisition and Utility Relocation | Final Design, ROW Acquisition and Utility Relocation | Bid | Construction | Construction | Construction |
| Placentia Avenue | UC | OCTA | Bid | Construction | Construction | Construction | | |
| Kraemer Boulevard | UC | OCTA | Bid | Construction | Construction | Construction | | |
| Orangethorpe Avenue | OH | OCTA | Final Design, ROW Acquisition and Utility Relocation | Bid | Construction | Construction | Construction | |
| Tustin Avenue/Rose Drive | OH | OCTA | Final Design, ROW Acquisition and Utility Relocation | Bid | Construction | Construction | Construction | |
| Lakeview Avenue | OH | OCTA | Final Design, ROW Acquisition and Utility Relocation | Final Design, ROW Acquisition and Utility Relocation | Bid | Construction | Construction | |


UC - undercrossing
OC - overhead

Legend:

-  Final Design, ROW Acquisition and Utility Relocation
-  Bid
-  Construction

Trade Corridors
Improvement Fund
(TCIF)
Construction
Must-Start Date

Placentia Avenue Undercrossing



O.C. BRIDGES

Improving safety. Removing delays.

@ Placentia Avenue

Orangethorpe Avenue Overpass



O.C. BRIDGES

Improving safety. Removing delays.

@ Orangethorpe Avenue

Next Steps

- Program Budget and Funding Update
- Design Contract Amendment
- Demolition Contract Procurements
- Cooperative Agreement Amendments with Cities
- Resolutions of Necessity for Lakeview Avenue ROW
- Construction and Maintenance Agreements with BNSF and the City of Placentia for Orangethorpe Avenue and Tustin Avenue/Rose Drive
- Request for Proposals for Lakeview Avenue Construction Management
- Invitation for Bids for Orangethorpe Avenue and Tustin Avenue/Rose Drive

Outreach Goals



Community Outreach



Get connected – Stay connected



OCTA – OC Bridges



OC Bridges



www.ocbridges.com / www.ocbridges.net



1-877-OCTA-999

Tresa Oliveri (714) 560-5374

