


San Diego Freeway (Interstate 5) Oso Parkway Interchange Improvement Project

Planned Improvements

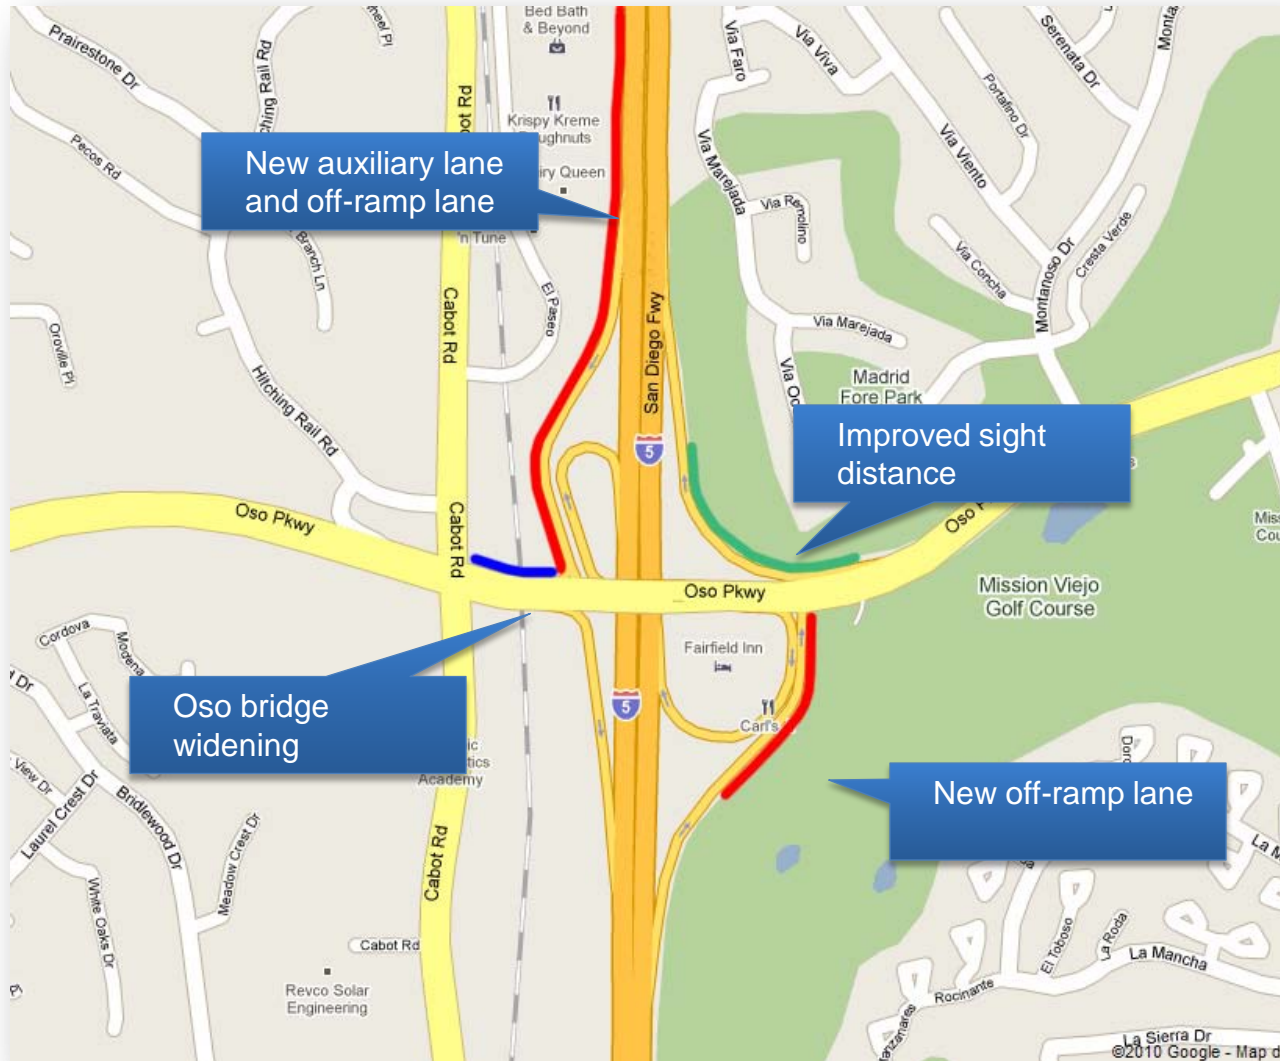

Project Overview

- Project funding
 - \$14.3 Million
 - State transportation improvement funds
- Construction schedule
 - Start - Sept 2008
 - Completion - July 2010

Southbound Off-Ramp



Northbound On-Ramp



Oso Parkway Bridge



Natural Gas Line Routing



Revised Project Schedule

- Open freeway ramps
 - May 2010
- Relocate natural gas line
 - November 2010
- Complete Oso bridge
 - August 2011
